

Official Proposal

40FT One-Trip Double Door + courtyard awning roof

Prepared for Chuck Galavich. We quoted \$4,400 delivered cash for one 40FT One-Trip Double Door. Chuck then asked us to roof across a 30-foot gap to a second unit with a traditional truss roof. Shingles or metal — whichever is cheaper.

Prepared for: Chuck Galavich

Delivery ZIP: 43719 Bethesda, Ohio (Belmont County)

Phone: 740-238-0492

Email: galavichchuck@gmail.com

Date: 19 August 2026

Prepared by: Christopher Banks, President/Owner

Company: CBGC LLC DBA CBShippingSolutions

Site: Two parallel units, 30 feet clear. Existing unit assumed 40FT until we have a photo.

COMPLETE CASH TOTAL

\$32,250.00

40FT One-Trip Double Door, delivered \$4,400.00

Courtyard awning roof, built \$27,850.00

These are complete cash totals. Standard weekday delivery of the container to a truck-accessible site is already inside the \$4,400. The awning figure is turnkey labor and materials for the roof described in this packet. Do not add freight on top.

The One-Trip box carries a 10-year structural and 10-year no-leak warranty. The awning is a site-built wood-and-metal structure warrantied 2 years workmanship. Metal panel finish follows the mill warranty.

CHEAPER ROOF

We priced a shingle roof and a metal roof on the same trusses. Metal 26-gauge R-panel on purlins is the cheaper complete system. Shingles need a full OSB deck, a 4:12 pitch, and more labor on an open awning. Metal stays at 3:12, skips the deck, and sheds better with wind under the roof. That is what this bid uses.

PART A — CONTAINER

- Furnish one 40FT One-Trip Double Door shipping container.
- Weekday delivery to a truck-accessible pad. Tilt-bed drop. Client grades the pad.
- Place the box parallel to the existing unit with 30 feet clear between the inner faces.
- End doors remain operable. No posts in the door swing.
- The \$4,400 already quoted is the delivered cash price for this box. It is not a starting point for a freight add-on.

PART B — COURTYARD AWNING


- Install pressure-treated 2x10 sleepers on both container roofs over an isolation membrane. Through-fasten to the top side rails with backing. Do not hang the roof from the roof skin alone.
- Set 22 engineered wood Fink trusses, 32-foot span, 3:12 pitch, 24 inches on center, covering the 40-foot boxes plus 12-inch overhangs each end (42 feet of roof).
- Install permanent bracing, hurricane ties, and 2x4 purlins.
- Install 26-gauge painted R-panel metal, ridge, eave, rake, closures, and gasketed screws.
- Install a simple 6-inch gutter and downspouts on both eaves so water does not dump on the courtyard or the box doors.
- Flash the sleeper-to-container joint so the existing roofs stay dry.
- Leave the courtyard open. No walls, no slab, no interior finish in this bid.
- Broom-clean the site. Haul scrap metal and lumber.

WHAT THIS IS NOT

This is not a building with walls. It is not a reroof of the container tops except at the sleeper and flash. Delivery is 43719 Bethesda, Ohio (Belmont County). Belmont County ground snow is in the light 20 psf class — the truss plant stamps the package to that local load. This is not a lake-effect or mountain snow upgrade. It does not include permits, a site PE stamp beyond the truss-plant package, concrete, electric, plumbing, or moving the existing box.

SHEET A1 PLAN NOT FOR CONSTRUCTION


Prepared for Chuck Galavich · 43719 Bethesda, Ohio

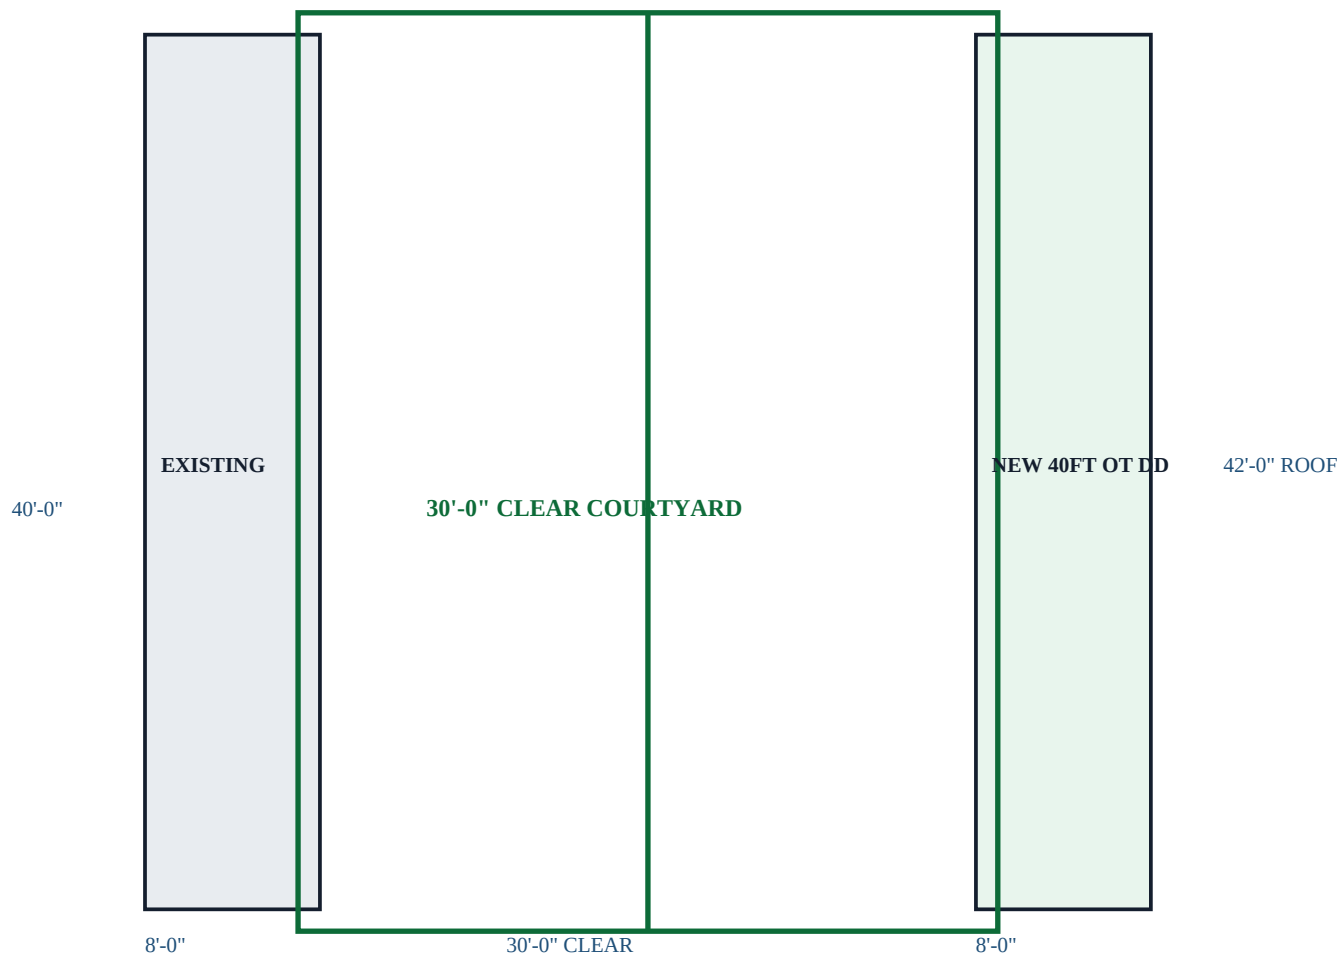

- NOTES
- Two 40FT boxes, parallel. New unit is a One-Trip Double Door.
 - Roof bears on PT sleepers on each container roof. Courtyard stays open.
 - Trusses at 24" O.C. 3:12 gable. 26-ga R-panel metal (cheaper complete system).
 - End doors stay clear. Do not block with posts.
 - Existing unit assumed 40FT. If shorter, roof trims to the shorter box.

SHEET A2 SECTION NOT FOR CONSTRUCTION


Prepared for Chuck Galavich · 43719 Bethesda, Ohio

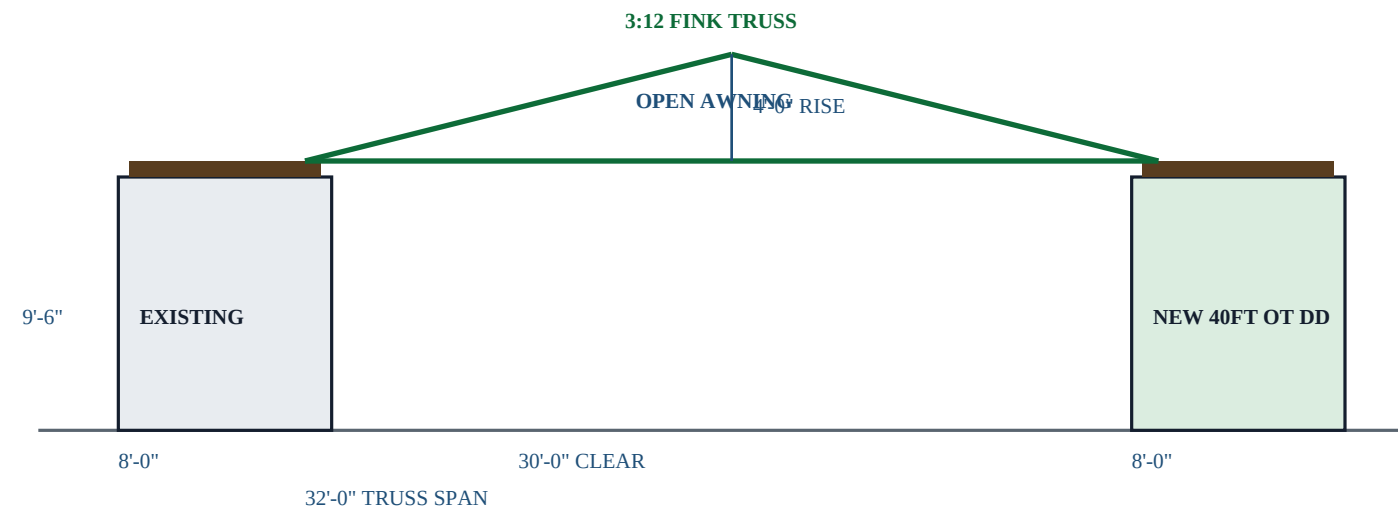

Sleepers are pressure-treated 2x10 on an isolation membrane, through-fastened to the top side rail — not to the roof skin only. Metal R-panel on 2x4 purlins. No OSB deck. That is why metal beats shingles on this open span.

SHEET A3 END ELEVATION NOT FOR CONSTRUCTION

View from the container ends. Courtyard stays open. No posts in the door swing.

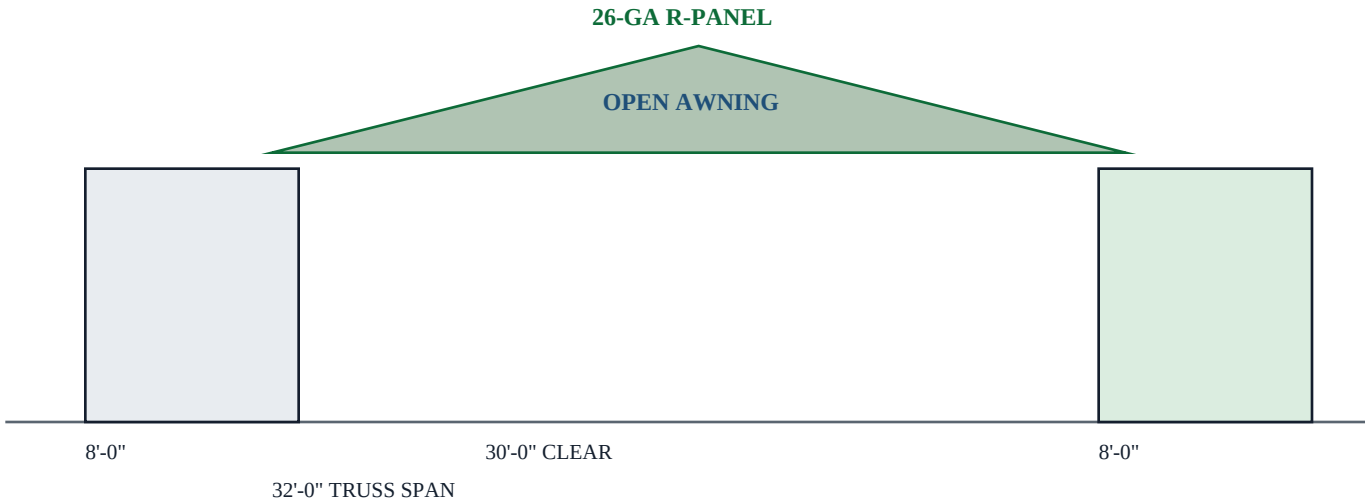

3:12 gable. Gutters at both eaves. Metal is the cheaper complete roof versus shingles on this span. Dimensions that govern the bid are on Sheets A1 and A2.

WHY METAL WINS

Same 22 trusses either way. Shingles need 4:12, a 7/16 OSB deck, underlayment, and more labor on an open span. Metal stays 3:12 on purlins. Installed, metal is the cheaper complete roof for this awning.

STRUCTURE TAKEOFF (contractor cost used to build the bid)

Engineered Fink trusses, 32' span, 3:12, 22 ea @ \$220	\$4,840
Truss-plant engineering / stamp	\$850
Truss freight to site	\$375
PT 2x10 sleepers, isolation membrane, through-bolts	\$980
Permanent bracing, ties, hangers	\$810
2x4 purlins	\$380
26-ga painted R-panel, ~1,500 sf with waste @ \$2.20	\$3,291
Ridge, eave, rake, closures, gasketed screws	\$980
6" gutter and downspouts, both eaves	\$672
Labor, lull / telehandler, set, metal, flash, cleanup	\$8,200
Direct cost	\$21,378

Direct cost \$21,378. Complete cash bid for the structure is \$27,850.00. The spread covers mobilization, small tools, waste, and the 2-year workmanship warranty. It is not an invitation to rebid the pieces.

SHINGLE ALTERNATE (not used)

If the client insisted on shingles: raise pitch to 4:12, add 48 sheets OSB, underlayment, 16.5 squares architectural shingles. Extra deck and labor runs about \$2,800–\$3,500 more installed. We are not bidding that unless you ask.

PRICING TERMS

40FT One-Trip Double Door, delivered cash	\$4,400.00
Courtyard awning roof, complete cash	\$27,850.00
Project total, complete cash	\$32,250.00

Quoted amounts are delivered cash prices. Standard weekday delivery of the container to a truck-accessible site is included in the container figure. The awning figure is a complete cash total for the labor and materials in this packet. Figures are not an invitation to separate or rebid cost pieces.

Home or farm drop: paid before the truck is dispatched and before the awning crew is scheduled. We do not collect on delivery. No COD.

NOT IN THIS NUMBER

- Permits, impact fees, or a site PE stamp if Belmont County wants more than the truss-plant package.
- Concrete, gravel pad, or moving the existing container.
- Electric, lights, or solar.
- Walls, roll-up doors, or closing in the courtyard.
- Weekend, crane, or off-road delivery.
- Ohio tax, if the state requires it on the container or any part of the work — billed as incurred. It is not inside these cash figures.

HOLD

This bid holds 14 days. Lumber and metal move. After 14 days we reconfirm the structure number. The \$4,400 on the box holds as already quoted unless the client changes size, grade, or doors.

SEQUENCE

- Chuck Galavich sends a photo of the existing box and the 30-foot gap, and confirms the pad will take a tilt-bed and a lull.
- We write the container order and collect before the truck.
- Box lands parallel, 30 feet clear, doors unobstructed.
- Truss package is ordered to the field measure (we verify 30 feet on the ground before we cut).
- Sleepers, trusses, purlins, metal, gutters, flash, clean.
- Two to four working days on the roof after the box is set, weather allowing.

WHAT WE NEED FROM YOU

ZIP 43719 is locked. We still need a photo of the existing unit and the 30-foot gap, whether that box is 20FT or 40FT, and how we access the pad. Belmont County may want a permit on a 32-foot span roof — we will say so before we collect.

CLOSE

IF you have any questions or concerns do not hesitate to reach out to me using the contact information below.

With thanks and my blessings!

Christopher Banks

President/Owner

Direct Business Line: (870)-682-3867

Personal Phone: (870)-323-2593

Website: [Https://cbshippingsolutions.com/](https://cbshippingsolutions.com/)
